

ServiceNow SPM Implementation (MVP) | Solution Design

Authors: Francisca Salgado (Deloitte) | email: frsalgado@deloitte.pt

Date: 13/03/2026

Summary:

Körber is implementing ServiceNow Strategic Portfolio Management (SPM) to standardize and strengthen the way R&D initiatives are managed across Business Areas (BAs). Today, processes, tools, and reporting are fragmented, limiting transparency, governance, and cross-functional prioritization.

SPM will establish a common foundation for Demand, Project, Portfolio Planning, and Reporting, enabling improved visibility, more consistent governance, and better data-driven decision-making. The solution is designed not only to support current needs, but also to provide a scalable and adaptable foundation for future portfolio management maturity and cross-BA innovation collaboration.

Contents

Introduction	3
Process Flow.....	4
Demand Lifecycle	4
States	5
Actions	5
Project Lifecycle.....	6
States	7
Actions	7
Personas and Responsibilities	8
Demand Creator	8
Demand Manager.....	8
Demand Approver	8
Project Manager	9

Portfolio Manager	9
RACI Matrix	9
Confidentiality and Access Model	10
Demand Form Overview	11
1. General Details.....	11
2. Organization	12
3. Business Case.....	13
4. Technology Insights.....	13
5. Financial Data/KPIs.....	14
Project Management.....	15
Project Form Overview.....	15
1. General Details.....	15
2. Organization	16
3. Dates	17
4. Business Case.....	17
5. Technology Insights.....	18
6. Financial Data / KPI	19
Example of How Financial KPIs Are Calculated Across the Project Timeline	20
Portfolio Planning	20
Breakdown Structure.....	20
Prioritization.....	23
Roadmap Planning.....	23
Financial Planning	24
Reporting and Dashboards	24

Introduction

This Functional Design Document describes the functional design for the implementation of the ServiceNow Strategic Portfolio Management (SPM) MVP at Körber.

The purpose of this initiative is to establish an initial, standardized foundation for managing Demands, Projects, Portfolio Planning, and Reporting across Körber's Business Areas. At present, R&D-related activities are managed through fragmented processes, tools, and reporting practices, which limits visibility across initiatives, reduces consistency in governance, and makes cross-functional prioritization more difficult.

To address this, Deloitte is implementing ServiceNow SPM as a common platform to support a more harmonized and transparent approach to portfolio management. The MVP scope is focused on enabling the core capabilities required to support the early stages of this transformation, while keeping the solution lean, practical, and scalable.

The design described in this document covers the initial functional scope agreed for the MVP, including:

- The management and evaluation of Demands;
- The definition of key Project data and lifecycle stages;
- The initial setup of Portfolio Planning capabilities;
- The enablement of Reporting and Dashboard views to support portfolio visibility and decision-making.

This solution design document follows an MVP approach with the objective of delivering value quickly through standard platform capabilities and a simplified data model. It is the starting point for the ServiceNow SPM implementation, followed by subsequent project phases to expand and mature the solution. The system's functionalities are intended to be **expanded and refined step by step** to ensure the software's readiness for operational use and automated interfaces with existing systems for importing external data. The requirements for future project phases will be compiled and followed up in an "Open Points List," followed by a proper evaluation, consolidation, and prioritization, which will be jointly aligned with all BAs and decided upon by the Steering Committee along with formal validation.

Process Flow

Demand Lifecycle

A Demand represents a **proposed initiative or business need** that requires evaluation before being approved for execution. It serves as the initial entry point for new initiatives within the portfolio management process.

At this stage, key business information is captured, such as the initiative's objectives, scope, expected benefits, and high-level financial considerations. The Demand lifecycle focuses on **qualifying the initiative** and ensuring that the required information is available to support governance decisions.

Before a Demand can be approved or rejected, it is typically reviewed by the relevant **decision committees**, which assess the initiative's strategic alignment, expected value, and feasibility. Based on this evaluation, the committee may approve the Demand to move forward or reject it.

Once a Demand has been approved, it can be converted into a Project, allowing the initiative to proceed to the execution phase.

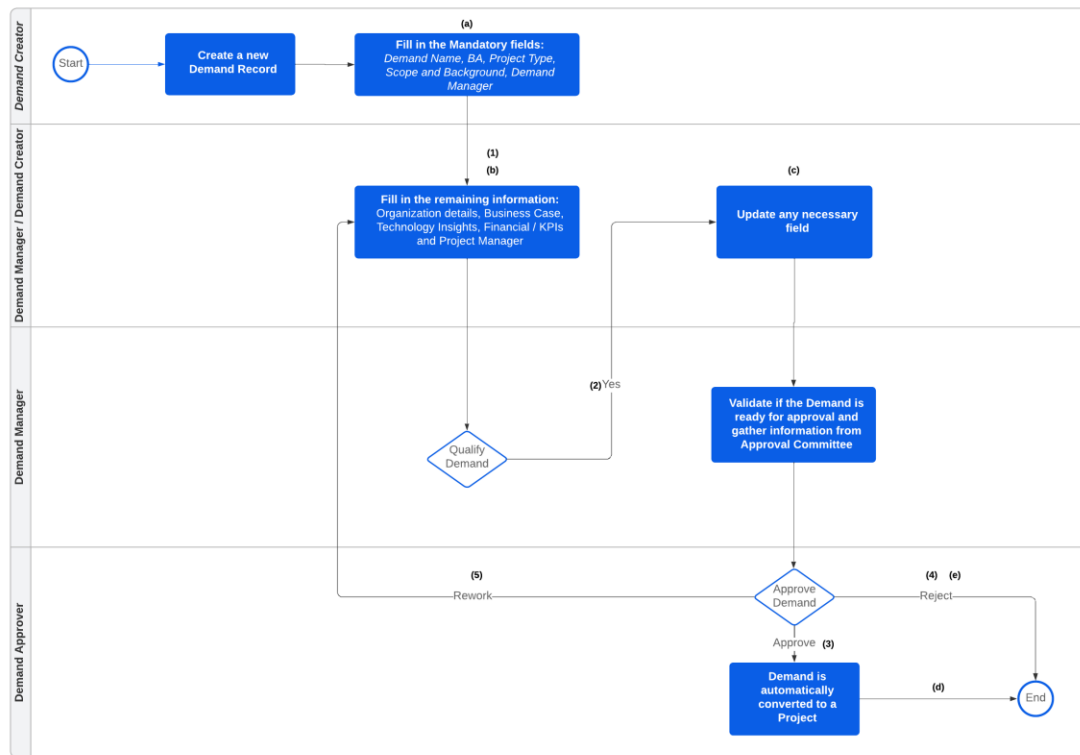


Figure 1 – Demand Lifecycle

States

State	Name	Description
(a)	Raised	Draft demand record with the mandatory information
(b)	Submitted	Demand formally submitted for qualification
(c)	Qualified	Demand reviewed and ready for approval assessment
(d)	Completed	Demand approved and converted into a project
(e)	Rejected	Demand not approved to move forward

Actions

Action	Name	Description
(1)	Submit demand	Submit the demand for qualification
(2)	Qualify	Confirm readiness for approval
(3)	Approve	Approve and convert demand into a project
(4)	Reject	Reject the demand
(5)	Rework	Return the demand to the submitted state

Project Lifecycle

A Project represents an approved initiative that has progressed beyond the demand evaluation phase and is ready for structured planning and execution.

During the Project lifecycle, detailed information is defined, including scope refinement, timelines, milestones, financial planning, and delivery readiness. The Project Manager is responsible for managing project activities, monitoring progress, and ensuring the initiative is delivered according to the defined objectives.

Throughout the project lifecycle, the initiative may pass through several **quality gates** and may be reviewed by **decision committees** to ensure continued alignment with strategic objectives, validate progress, and confirm readiness to proceed to the next phase.

The project lifecycle concludes with the formal closure of the initiative once the planned outcomes have been delivered.

In addition, for projects that are not in a pending status, if no updates are made for a period of one month, a notification will be triggered to alert the Project Manager that the project has not been updated during that time.

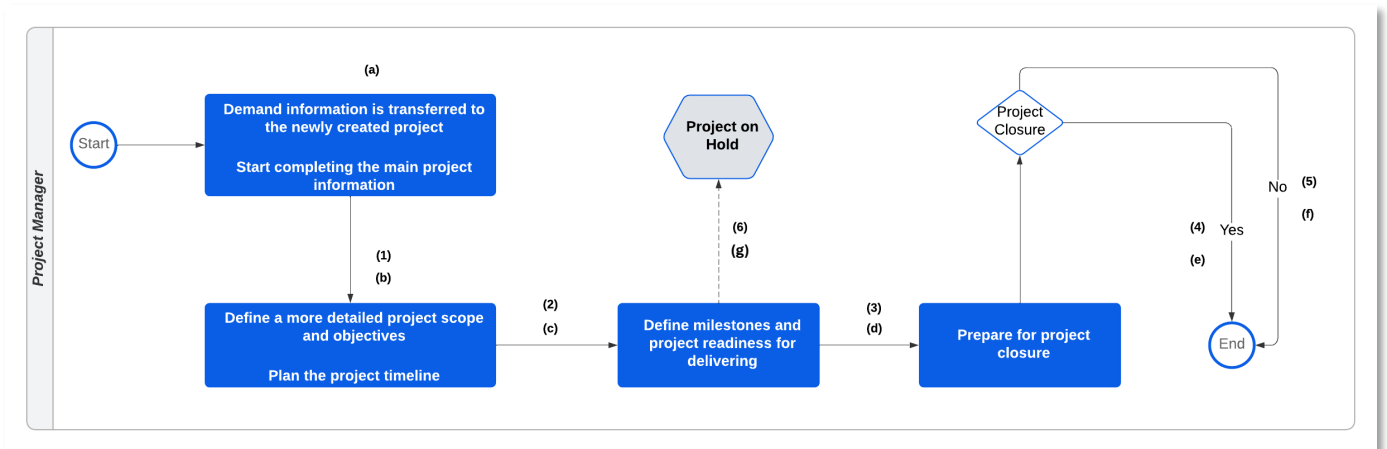


Figure 2 - Project Lifecycle

States

State	Name	Description
(a)	Open	Change state from pending to open when starting to fill information
(b) (c) (d)	Work in Progress	The project information is getting updated
(e)	Closed complete	Project is successfully closed
(f)	Closed incomplete	Project was cancelled
(g)	Pending	Project is on hold

Actions

Action	Description
(1)	Change initiating phase to planning
(2)	Change planning phase to executing
(3)	Change executing phase to delivering
(4) (5)	Change delivering phase to closing
(6)	Change state to pending

Personas and Responsibilities

The MVP solution is based on a set of key personas that support the lifecycle of Demands, Projects, and portfolio oversight activities. Each persona has a defined role in maintaining data quality, progressing initiatives, and supporting governance decisions.

Demand Creator

The Demand Creator is responsible for initiating the Demand record and completing the mandatory information required to register a new initiative. This includes the initial business and contextual information necessary to start the demand evaluation process.

In addition, the Demand Creator may update the Demand form and maintain the information contained in the record as needed. However, this role is not responsible for progressing the Demand through its lifecycle or for taking qualification or approval-related decisions.

Demand Manager

The Demand Manager is responsible for progressing the Demand through its evaluation lifecycle. This includes updating the necessary information, qualifying the Demand, validating whether it is ready for approval, and consolidating the information required for the approval process. The Demand Manager plays a central role in ensuring that Demand records are sufficiently complete and consistent before being redirected to the Demand Approver for approval and potential conversion into a Project.

Demand Approver

Once the Demand has been validated by the Demand Manager, the Demand Approver evaluates the information provided, confirms whether the initiative should move forward, and formally approves, rejects, or returns the Demand for rework.

If approved, the Demand is automatically converted into a project, allowing the initiative to move into the project management phase.

Project Manager

The Project Manager is responsible for managing the Project once a Demand has been approved and converted. Main responsibilities include completing the main project information, updating the financial data, refining scope and objectives, planning the timeline, defining milestones, preparing the project for delivery, and leading closure activities. The Project Manager is the main owner of project execution and delivery readiness.

Portfolio Manager

The Portfolio Manager is responsible for overseeing the portfolio of initiatives, ensuring alignment with strategic objectives, supporting prioritization decisions, and monitoring portfolio performance through planning and reporting views. Within the MVP, this role is primarily supported through dashboard visibility, portfolio planning capabilities, and reporting insights.

RACI Matrix

Demand

RACI Matrix

RACI Definitions		Primary responsibilities					
R = Responsible		Executes the activities identified to complete the work package as defined by the A. Drives the execution activities to success within the agreed upon timelines.					
A = Accountable		Understands and defines the activities needed to be executed to complete the work package successfully. Provides clear direction on scope and timelines to complete the activities.					
C = Consulted		Provides insight and is a Subject Matter Expert who provides expertise and knowledge to drive the activities to completion. Required to be an active participant in all impacted work package activities					
I = Informed		Requires knowledge of the activities being executed but is not an active participant in the completion of the activities. Output of the work package may have a downstream impact where the I requires knowledge for their role.					

ID	Activity	Demand Creator	Demand Manager	Demand Approver	Project Manager	Portfolio Manager	Subject Matter Expert (SME)
Demand							
D1	Create Demand	R/A	I	-	-	-	
D2	Complete required business case information (scope, value, risk)	R	A	I	-	I	C
D3	Approve/ Reject/ Defer Demand	I	A	R	-	I	

Figure 3 - Demand - RACI Matrix

Project and Portfolio

RACI Matrix

ID	Activity	Demand Creator	Demand Manager	Demand Approver	Project Manager	Portfolio Manager
Project						
P1	Initiating - Start completing the main project information	-	I	-	R/A	I
P2	Planning - Define a more detailed project scope and objectives and plan the project timeline	-	-	-	R/A	C
P3	Execute - Update financial data accordingly to the project's progress and plan and execute Quality Gate cycles	-	-	-	R/A	I
P4	Delivering - Finalize the remaining deliverables and prepare the project for closure	-	-	-	R/A	C
Portfolio						
F1	Maintain portfolio breakdown structure / taxonomy (categories, filters)	-	-	-	-	R/A
F2	Prioritize items (apply prioritization in plan)	-	C	C	C	R/A
F3	Roadmap sequencing (timeline fit, dependencies)	-	-	C	C	R/A

Figure 4 - Project - RACI Matrix

Confidentiality and Access Model

The MVP includes a confidentiality-based access model designed to balance transparency, controlled visibility, and collaboration across Business Areas. Confidentiality is defined at **individual Demand and Project record level**, according to the sensitivity of each initiative, rather than being applied as a single global setting across the platform.

As part of the initial implementation approach, all **ongoing Demands and Projects migrated into the system** will be set to **Confidential** by default, ensuring a controlled baseline during transition. For all **new Demands and Projects**, the **Confidentiality Level** will be a **mandatory field** and no preselected value will be applied. Users will therefore be required to actively select the confidentiality level that they consider most appropriate for each initiative.

The model supports three confidentiality levels, complemented by an additional **Collaborators** mechanism for controlled visibility exceptions. These exceptions will be proposed by Deloitte and presented to Körber until the 23rd of March.

The confidentiality level is configured per Demand/Project record and can vary depending on the sensitivity of each initiative.			
Confidential level field			Collaborators field
(1) Public (Default – Recommended Baseline)	(2) Confidential	(3) Strictly Confidential	Extra Layer – Collaborators
- Visible to all business users within each BA with SPM access - Sensitive fields (e.g., detailed financial data) may be restricted per default - Promotes cross-Business Area transparency, collaboration, and identification of synergies - The speed of delivery of each process is conditioned by the responsiveness of the process stakeholders Recommendation: Public should be the default setting to foster transparency and organizational coherence, while avoiding unnecessary complexity and fragmentation of the portfolio view.	- Visible only to users within the associated Business Area - Other Business Areas do not have access to detailed information - Protects sensitive operational or strategic initiatives within a specific Business Area Additional protection: sensitive fields are hidden from non-authorized users Recommendation: Confidential should be used for initiatives that contain sensitive information and require visibility restricted to the associated BA.	- Access limited to: - The demand manager / project manager / portfolio manager - Explicitly designated users - Intended for highly sensitive initiatives Additional protection: sensitive fields are hidden from non-authorized users Recommendation: Strictly Confidential should be reserved for exceptional cases involving highly sensitive initiatives where access must be limited to the demand manager / project manager / portfolio manager only.	- Allows specific users to be granted visibility beyond the default confidentiality setting - Enables flexibility without altering the core access model - Supports cross-functional collaboration when required - Ensures that governance bodies can access relevant initiatives without broadening general visibility Recommendation: Collaborators should be used to grant specific users visibility beyond the set confidentiality level, allowing controlled exceptions when collaboration is required.

Figure 5 - Confidentiality Level per demand / project

Demand Form Overview

The Demand form is divided into several actions to streamline navigation and help users quickly find the information they need. These sections include:

1. General Details

This section captures the essential information that defines and contextualizes the demand at a high level:

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
General Details	Number	Unique identifier automatically assigned to each demand.		X	X	Automatically generated when a new demand is created. The number follows the format DMNDxxxx and is sequentially incremented
	Demand Name	Title of the demand.	X			Should clearly identify the demand
	Business Area	Business Area related to the demand. (Technologies, Pharma , Supply Chain)		X	X	Automatically populated based on the business area of the user creating the demand.
	Project Type	Classification of the project type.	X			Multiple choice: Sustain (PLD-S), Upgrade (PLD-U), Evolution (PND), Disruption (PND), Exploration (TPD)
	Tech Stack	Technology domain related to the demand	X			Multiple Choice: Hardware, Software, Digital & AI

State	Field	Description	Mandatory	Read only	Automation	Observations
General Details	Demand Manager	Responsible for reviewing, qualifying, and progressing the demand	X			The available Demand Managers are filtered based on the selected Business Area and Business Unit
	Project Manager	Manager responsible for reviewing, qualifying, and progressing the project	X			Mandatory during the qualification process
	State	Current lifecycle status of the demand.			X	States: Raised, Submitted, Qualified, Rejected, Completed
	Start Date	Start date of the demand				Used for high-level demand planning
	Due Date	Due date of the demand				
	Project Planned Start Date	Planned start date of the project				Used for high-level project planning
	Project Planned End Date	Planned end date of the project				
	Portfolio	Portfolio to which the demand belongs to manage related initiatives			X	Automatic to the specific Business Area

Figure 6 - General details of the Demand

2. Organization

This section identifies the organizational structure and classification elements associated with the demand:

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Organization	Business Unit	Business unit responsible for the demand			X	Available options depend on the selected Business Area. Technologies: Primary, Secondary, Specialized Solutions, Services Pharma: Machinery, Software, Materials Supply Chain: Automation, Parcel, Automation+Parcel Note: Product categories and families with in Supply Chain are currently under review and may be adjusted.
	Product category	Product category within each Business Unit			X	The product category will be defined depending on the select Business Unit
	Product Family	Displayed only when Business Area is KSC.			X	The Product Family options will automatically be displayed according to the selected Category.
	Company	Legal entity associated with the demand			X	The Company options choice will be automatically defined based on the selected Business Area

Figure 7 - Organization of the Demand

3. Business Case

This section captures the justification, context, and scope definition necessary to understand the purpose and impact of the demand:

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Business Case	Opened by	User who created the demand record in the system.		X	X	Automatically populated when the demand is created.
	Collaborators	Users involved in contributing to the demand definition				Depending on the confidentiality level, members outside the BA (with SPM user license) can access and update the Demand.
	Scope and Background	Description of the business need	X			Provides the rationale and context for the proposed initiative.
	Risk of not doing	Business, operational, financial, or strategic risks if the demand is not implemented.				Helps assess the impact of not proceeding with the initiative
	In scope	Defined deliverables, functionalities, or business areas included in the demand.				Clarifies what is included within the scope of the initiative
	Out of scope	Explicit exclusions to clarify boundaries and avoid scope creep.				Clarifies what is not included within the scope of the initiative

Figure 8 - Business Case of the Demand

4. Technology Insights

This section captures the technology-related aspects of the demand, ensuring alignment with AIR initiatives and innovation themes:

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Technology Insights	Focus Technology	Description of the technology				Open text field.
	AIR Project	Indicates whether the demand is related to an AIR initiative	X			Yes/No field used to identify AIR-related initiatives
	AIR Theme	Classification of AIR Theme	X		X	Visible only when "AIR Project" = Yes. Available values: Automated, Regenerative, Intelligent.
	Innovation Cluster	Categorizes the demand according to the strategic innovation domain it contributes to.	X		X	Visible only when "AIR Project" = Yes. Filtering: The list of available values is automatically filtered according to the selected AIR Theme. Automated: - Robotics & Autonomous Systems - Smart Material Handling - Perception & Sensing - Process Automation & Workforce Enablement Intelligent: - AI-Driven Optimization & Decision Systems - Digital Twins & Virtualization - Unified Factory Control - Industrial IoT & Secure Connectivity Regenerative: - Servitization & XaaS Models - Circular Economy - Energy-Efficient & Carbon-Neutral Manufacturing - Smart & Sustainable Materials

Figure 9 - Technology Insights of the Demand

5. Financial Data/KPIs

This section captures all financial inputs and outcome-based KPIs necessary to estimate benefits, costs, and overall value of the demand.

Note: All Financial Data/KPIs are captured on a yearly basis. Following market launch, data must be entered for each of the five subsequent years. For further clarification, see Figure 17 on page 20.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Financial Data/KPIs	Number of machines sold	Hint: Expected number of machines to be sold annually				
	Unit price	Expected price to be defined based on the market				
	Revenue	Revenue from selling products / solutions in the time period of 5 year after market launch			x	Number of machines sold × Unit price.
	Cost Savings	Expected cost reduction in the time period of 5 year after market launch				Benefit of manufacturing / design cost reduction
	Total planned benefit (rough estimation)	Hint: Total planned benefit estimation per year Equal to Revenue + Cost Savings			x	Sum of Revenue and Cost savings
	R&D Costs	Costs related to engineering and development activities in the time period of 5 year after market launch				Used to breakdown the Total Planned Cost
	Manufacturing Costs	Per unit				
	Other Costs	(e.g. Market launch, serial design costs and other relevant costs)				
	Total Planned Cost (rough estimation)	Hint: Total costs estimation per year in the time period of 5 year after market launch			x	Sum of R&D costs, Total Manufacturing costs, and other Costs.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Financial Data/KPIs	EBIT	Hint: Total Planned Benefit – Total Planned Cost			x	The value will be displayed in euros (€) .
	CM1 %	Hint: (EBIT/Total Planned Benefit)*100			x	Contribution margin
	ROI %	Hint: ((Total Planned Benefit – Total Planned Cost) / Total Planned Cost) * 100		X	x	Return on Investment calculated based on the estimated benefits and costs
	Net present value	Planned benefit/ (1+i) ^t i = Interest Rate % [For NPV] t = number of periods		X	x	Present value of future benefits discounted over time in euros (€) .
	Interest Rate % [For NPV]	Hint: Fixed value defined by Körber		X	x	Fixed value: 10%
	Strategic Intent	Strategic objective				Options: Market driven / Customer driven
	Impact Type	Type of business impact expected from the initiative				Options: Growth Cost reduction Protect core business

Figure 10 – Financial KPIs of the demand

Project Management

Project Form Overview

The Project form was organized into multiple sections to improve navigation and ensure users can quickly locate relevant information. Sections include:

1. General Details

The *General Details* section captures the core identifying information of a project. These fields define the project's fundamental attributes, such as its unique identifiers, classification, and business context, and serve as the basis for reporting, governance, and alignment with the originating demand.

All fields in this section are **automatically inherited from the Demand** to ensure data quality and avoid manual rework, but they remain **editable** if adjustments are needed.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
General Details	Number	Unique identifier automatically assigned to each project.		X	X	Automatically generated when a new project is created. The number follows the format PRJxxxx and is sequentially incremented
	Project ID-number	Unique business identifier for the project.				Free text field
	Project Name	Title of the project.	X			Should clearly identify the project.
	Business Area	Business Area related to the project. (Technologies, Pharma , Supply Chain)		X	X	All this information is inherited from the Demand level.
	Project Type	Classification of the project type.	X		X	
	Tech Stack	Technology domain related to the project.	X		X	

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
General Details	State	Current lifecycle status of the project.			X	States: Pending, Open, Work in Progress, Closed Complete, Closed Incomplete
	Project Manager	Manager responsible for reviewing, qualifying, and progressing the project.	X		X	This information is inherited from the Demand level
	Portfolio	Portfolio to which the Project belongs to manage related initiatives			X	Automatic to the specific Business Area
	Project Sponsor	Serves as the main escalation and decision contact.				Open field or list of predefined users

Figure 11 - General details of the project

2. Organization

The Organization section defines the organizational context of the project, capturing key information such as the business unit, product category, product family, and company.

These fields ensure alignment between the originating Demand and the project record, enabling consistent reporting, governance, and financial traceability.

All fields in this section are **automatically inherited from the Demand** to ensure data quality and avoid manual rework, but they remain **editable** if adjustments are needed.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Organization	Business Unit	Business unit responsible for the project.			X	All this information is inherited from the Demand level.
	Product category	Product category within each Business Unit			X	
	Product Family	Displayed only when Business Area is KSC.			X	
	Company	Legal entity associated with the project			X	

Figure 12 - Organization of the project

3. Dates

The Dates section captures the key planned and actual timeline milestones of the project. These fields support schedule management, baseline tracking, and alignment between the initial demand assessment and the project execution lifecycle.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Dates	Planned start date	Planned start date of the project		X	X	All this information is inherited from the Demand level
	Planned end date	Project end date of the project		X	X	
	Actual start date	Actual date when the project execution begins				Date when the project officially starts
	Actual end date	Actual date when the project is completed			X	Date when the project is closed

Figure 13 - Dates of the project

4. Business Case

The *Business Case* section captures the rationale, context, and strategic relevance of the project. These fields provide visibility into the business need, associated risks, and project scope boundaries. Much of the information originates at the Demand level and is automatically carried over to the Project to maintain consistency across the intake and delivery lifecycle.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Business Case	Opened by	User who created the project record in the system.		X	X	Automatically populated when the project is created.
	Collaborators	Users involved in contributing to the project definition				Users involved in contributing to the definition and progress of project.
	Scope and Background	Description of the business need			X	Provides the rationale and context for the current project. The data captured in these field at the Demand level will be automatically carried over to the Project level.
	Risk of not performing	Business, operational, financial, or strategic risks if the project is not implemented.			X	The data captured in these field at the Demand level will be automatically carried over to the Project level.
	Risk of performing	Business, operational, financial, or strategic risks associated to the project's implementation.				Helps to anticipate issues and reduce potential project impact.
	In scope	Defined deliverables, functionalities, or business areas included in the project.			X	The data captured in these field at the Demand level will be automatically carried over to the Project level.
	Out of scope	Clarifies what is not included within the scope of the project			X	

Figure 14 - Business Case of the project

5. Technology Insights

The *Technology Insights* section captures technology related classifications that -help identify the technological domain, AIR relevance, and innovation context of the project. **All fields in this section are inherited from the originating Demand** to ensure consistency and prevent misalignment between intake and delivery stages.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Technology Insights	Focus Technology	Description of the technology			X	All this information is inherited from the Demand level.
	AIR Project	Indicates whether the project is related to an AIR initiative	X		X	
	AIR Theme	Classification of AIR Theme	X		X	
	Innovation Cluster	Categorizes the project according to the strategic innovation domain it contributes to.	X		X	

Figure 15 - Technology Insights of the project

6. Financial Data / KPI

The *Financial Data / KPIs* section consolidates the project's expected financial performance, cost structure, strategic impact, and investment indicators. These fields support business case evaluation, cost–benefit analysis, and financial tracking throughout the project lifecycle. **All values captured at the Demand stage are automatically transferred to the Project record** to ensure alignment between intake assessment and execution. Computed financial indicators are system driven and update dynamically when underlying values change.

Note: All Financial Data/KPIs are captured on a yearly basis. Following market launch, data must be entered for each of the five subsequent years. For further clarification, see Figure 17 on page 20.

Cluster	Field	Description	Mandatory	Read-Only	Automation	Observations
Financial Data/KPIs	*Number of machines sold	Hint: Expected number of machines to be sold annually				
	*Unit price	Expected price to be defined based on the market				
	*Revenue	Revenue from selling products / solutions			x	Number of machines sold x unit price.
	*Cost Savings	Reduction of planned expenses				Benefit of manufacturing / design cost reduction
	*Total planned benefit	Hint: Total planned benefit estimation per year Equal to Revenue + Cost Savings			x	Sum of Revenue and Cost savings
	*R&D Costs	Research and development costs				
	*Manufacturing Costs	Per unit				Used to breakdown the Total Planned Cost
	*Other Costs	(e.g. Market launch, serial design costs and other relevant costs)				
	Total Planned Cost	Hint: Total costs estimation per year Equal to the Sum of R&D costs, Manufacturing costs, and other Costs.			X	Sum of R&D costs, Manufacturing costs, and other Costs.
	*EBIT	Total Planned Benefit – Total Planned Cost			X	The value will be displayed in euros (€) .
	*CM1 %	Contribution margin			X	
	ROI %	Hint: $((\text{Total Planned Benefit} - \text{Total Planned Cost}) / \text{Total Planned Cost}) * 100$		X	X	Return on Investment calculated based on the estimated benefits and costs
	Net present value	Planned benefit/ $(1+i)^t$ i = discount rate t = number of periods		X	X	Present value of future benefits discounted over time in euros (€) .
	Interest Rate % [For NPV]	Hint: Fixed value defined by Körber		X	X	Fixed value: 10%
	Strategic Intent	Strategic objective				Options: Market driven / Customer driven
	Impact Type	Type of business impact expected from the initiative				Options: Growth / Cost reduction / Protect core business

Figure 16 - Financial KPIs of the Project

Example of How Financial KPIs Are Calculated Across the Project Timeline

The table below provides an illustrative example of how the financial metrics are calculated across both the development period and the projected five-year post-launch timeframe.

	Development Time ...		5-years forecast after market launch				
	2025	2026	2027	2028	2029	2030	2031
# machines sold	0	0	2	4	6	8	10
Price per machine	0	0	1,000	1,200	1,200	1,400	1,400
Revenue	0	0	2,000	4,800	7,200	11,200	14,000
Cost Savings	0	0	0	0	0	0	0
Total planned benefit	0	0	2,000	4,800	7,200	11,200	14,000
R&D Costs	-800	-600	-100	0	0	0	0
Manufacturing Costs	0	0	-300	-600	-900	-1,200	-1,500
Other Costs	0	-100	-100	-100	-100	-100	-100
Total Planned Costs	-800	-700	-500	-700	-1,000	-1,300	-1,600
EBIT (accumulated)	-800	-700	1,500	4,100	6,200	9,900	12,400
CM1	0%	0%	75%	85%	86%	88%	88%
ROI							
Net Present Value							

Figure 17 - Financial metrics per year during 5 years after market launch

Portfolio Planning

Portfolio Planning is included in the MVP as an initial capability to support higher-level planning and visibility across initiatives. Within the scope of this phase, the objective is to provide a structured view of portfolio items and enable an initial planning perspective across prioritization, roadmap visualization, and financial oversight.

The Portfolio Planning capability supports a more consolidated approach to evaluating and organizing initiatives within a portfolio context. It is intended to help stakeholders review the pipeline of work, assess planning items from a portfolio perspective, and support more informed decisions on sequencing, timing, and investment visibility.

Breakdown Structure

The breakdown structure provides the organizational view used to arrange and visualize portfolio items within the planning workspace.

Within the MVP, this structure can be configured within each Business Area to group planning items according to different business dimensions.

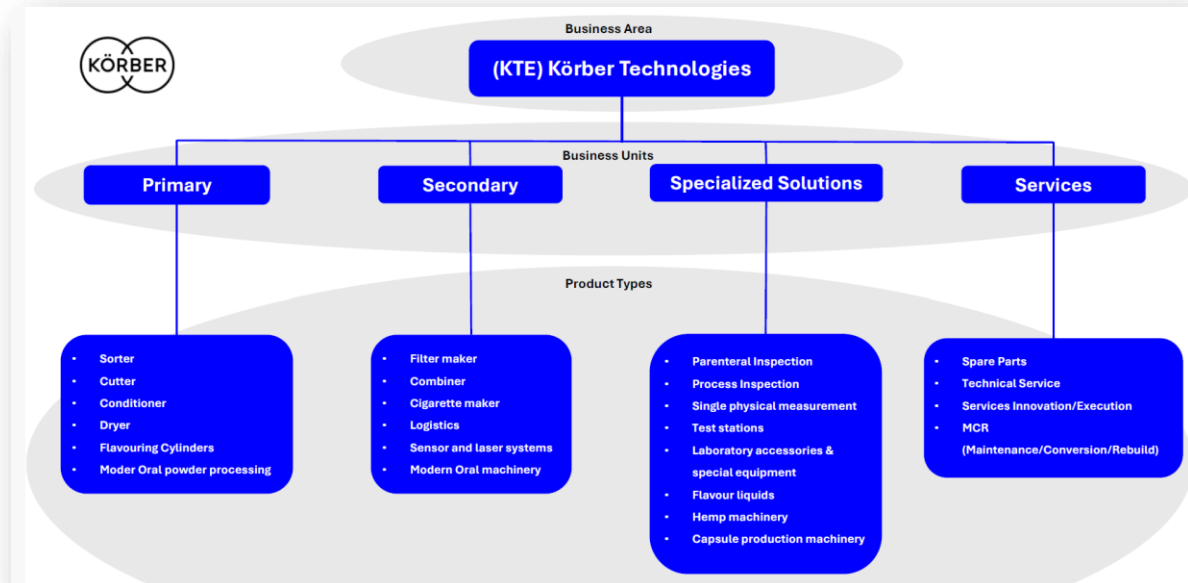


Figure 18 - KTE Breakdown Structure (structure decided for the MVP, possible changes may be applied)

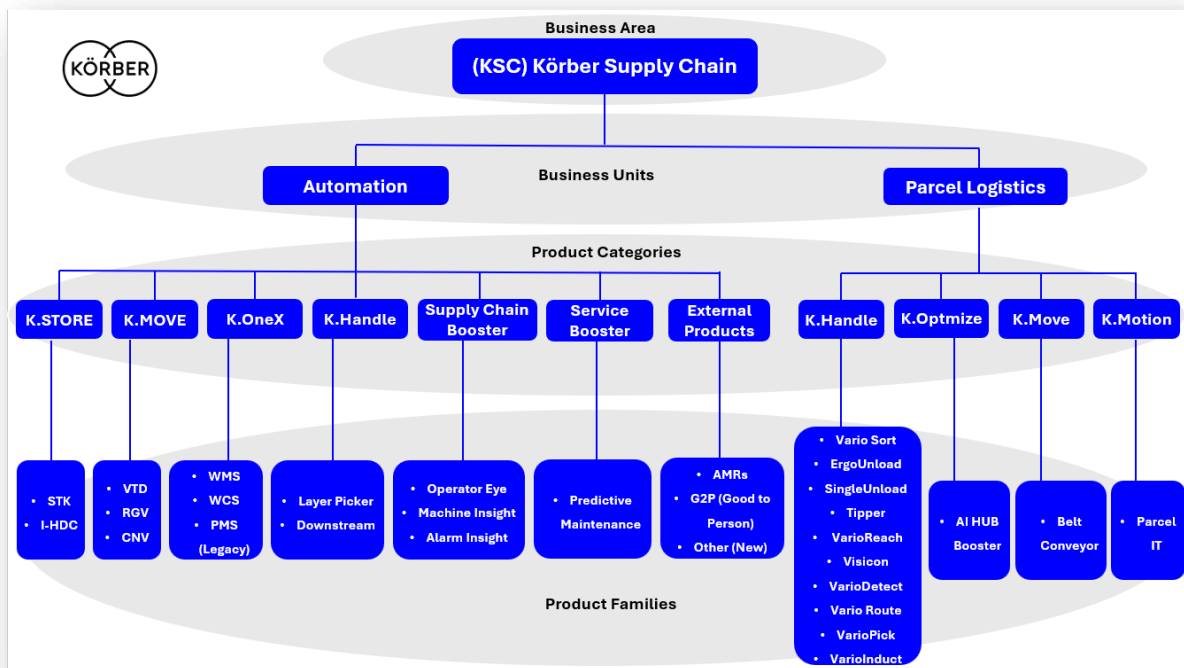


Figure 19 - KSC Breakdown Structure (structure decided for the MVP, possible changes may be applied)


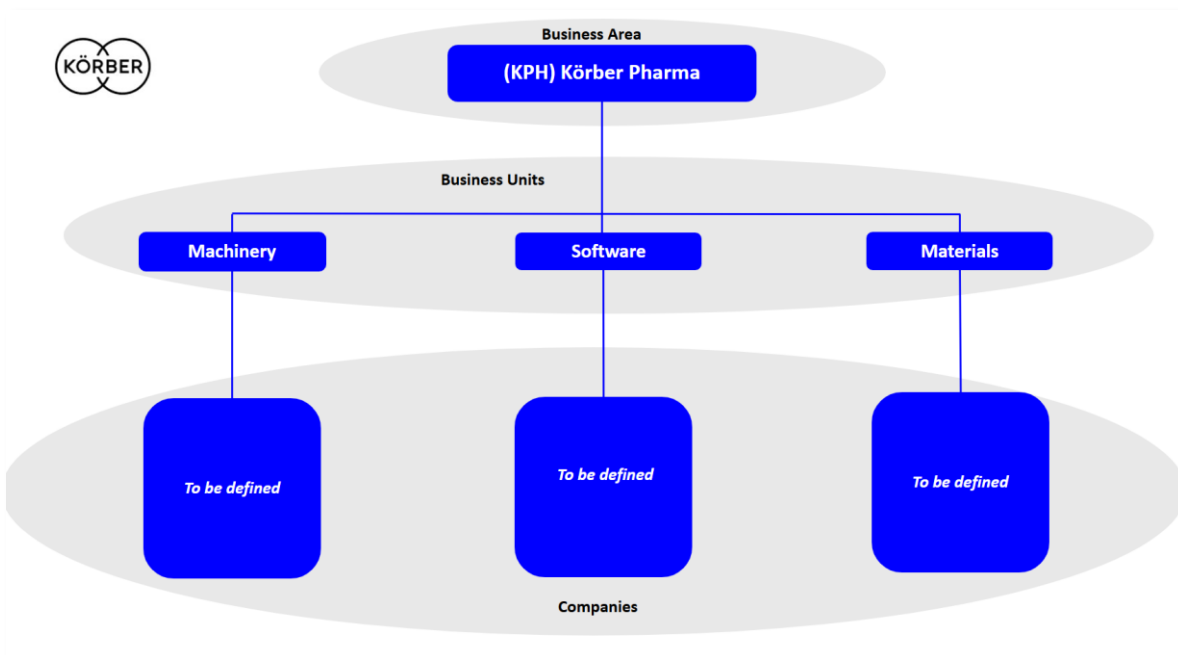


Figure 20 - KPH Breakdown Structure (structure decided for the MVP, the companies and product categories to be added)

Prioritization

The Prioritization component supports the initial review and assessment of portfolio items by providing a consolidated view of relevant Demands and Projects within the portfolio context. Within the MVP, it is intended to help stakeholders identify the work items under consideration, review them in a centralized planning view, and support prioritization decisions based on their relevance, value, and planning context. In this view, initiatives can be visualized using key attributes such as **Project Name, Business Area, Business Unit, Project Category, Status, Budget, Actual Costs, and ROI**, thereby contributing to a more structured portfolio-level review process.

Additional columns and filters can also be configured, allowing the view to be adapted to the data points most relevant for portfolio planning and decision-making.

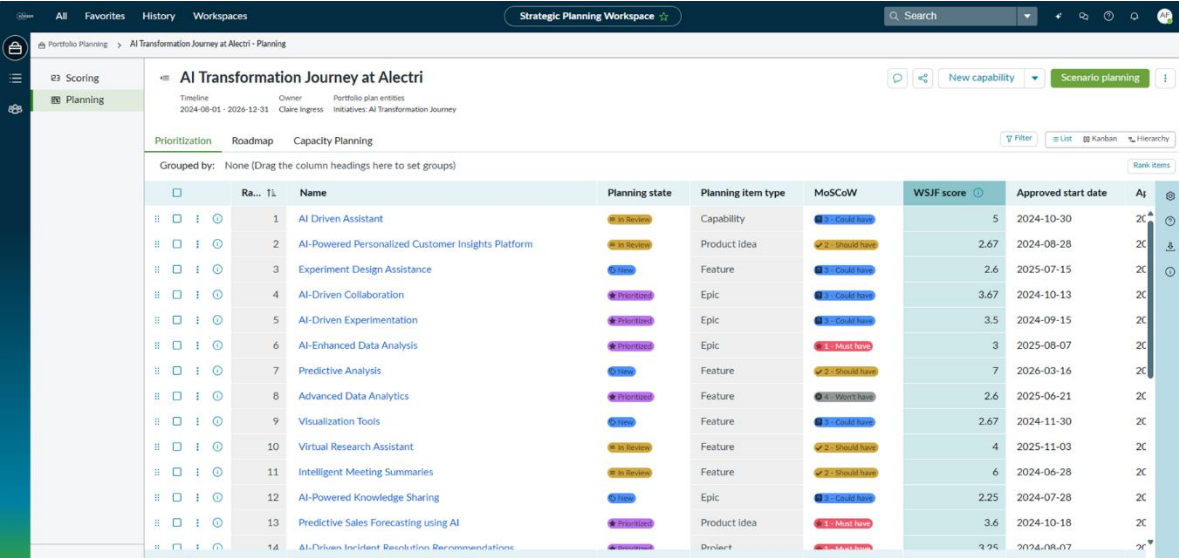

Rank	Name	Planning state	Planning item type	MoSCoW	WSJF score	Approved start date	Drag handle
1	AI Driven Assistant	In Review	Capability	1 - Must have	5	2024-10-30	2K
2	AI-Powered Personalized Customer Insights Platform	In Review	Product Idea	2 - Should have	2.67	2024-08-28	2K
3	Experiment Design Assistance	In Review	Feature	1 - Must have	2.6	2025-07-15	2K
4	AI-Driven Collaboration	In Review	Epic	2 - Should have	3.67	2024-10-13	2K
5	AI-Driven Experimentation	In Review	Epic	1 - Must have	3.5	2024-09-15	2K
6	AI-Enhanced Data Analysis	In Review	Epic	1 - Must have	3	2025-08-07	2K
7	Predictive Analysis	In Review	Feature	2 - Should have	7	2026-03-16	2K
8	Advanced Data Analytics	In Review	Feature	2 - Should have	2.6	2025-06-21	2K
9	Visualization Tools	In Review	Feature	2 - Should have	2.67	2024-11-30	2K
10	Virtual Research Assistant	In Review	Feature	2 - Should have	4	2025-11-03	2K
11	Intelligent Meeting Summaries	In Review	Feature	2 - Should have	6	2024-06-28	2K
12	AI-Powered Knowledge Sharing	In Review	Epic	1 - Must have	2.25	2024-07-28	2K
13	Predictive Sales Forecasting using AI	In Review	Product Idea	1 - Must have	3.6	2024-10-18	2K
14	AI-Driven Incident Resolution Recommendations	In Review	Product Idea	1 - Must have	1.25	2024-08-17	2K

Figure 20 - Example of Prioritization of demands and projects

Roadmap Planning

The Roadmap component provides a visual planning perspective over the initiatives included in the portfolio, supporting a high-level view of when work is expected to take place and how initiatives are positioned over time. Within the MVP, it is intended to provide an initial timeline-based view of portfolio items, enabling stakeholders to understand the overall planning horizon, support planning discussions across the portfolio, and improve coordination and visibility without serving as a detailed execution scheduling tool. In addition, the

roadmap can display dependencies between projects, supporting clearer sequencing and coordination across initiatives.

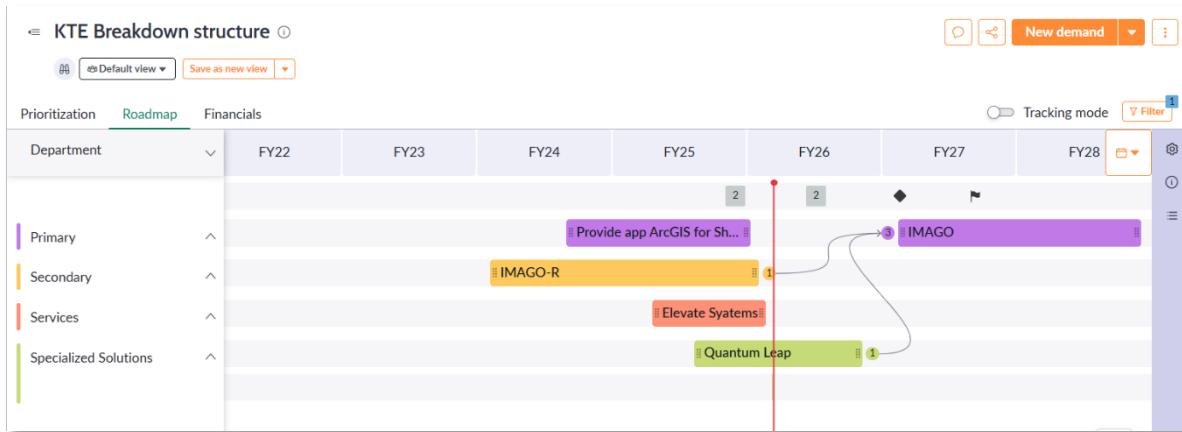


Figure 21 – Exemplary overview of project dependencies within the portfolio. Additional levels of structuring will be available, including the breakdown by product categories and other portfolio dimensions

Financial Planning

The Financial Planning component supports the portfolio view of financial information associated with planning items and is intended, within the MVP, to provide high-level visibility over planned and actual financial values. This capability enables stakeholders to review financial information from a portfolio planning perspective, supports the consolidation of cost-related views across initiatives, and provides an initial basis for portfolio monitoring, financial control, and decision-making, with the possibility for future expansion in later phases.

Reporting and Dashboards

Reporting and dashboard capabilities form an integral part of the ServiceNow SPM MVP, supporting visibility, monitoring, and decision-making across Demands, Projects, and portfolio planning activities.

Within the MVP scope, the reporting layer is intended to provide high-level portfolio visibility through summary indicators, dashboard-based views, and analytical perspectives that support portfolio governance. These capabilities are designed to enable consolidated visibility over Demand and Project information, support

monitoring of key financial and operational indicators, and provide management with a clearer view of the portfolio landscape.

From a functional perspective, the reporting and dashboard layer is intended to support the following objectives:

- Provide consolidated visibility over Demand and Project data;
- Support monitoring of financial and operational portfolio indicators;
- Enable analysis of initiatives across Business Areas and relevant classifications;
- Support management reporting through dashboard-based views.

Further detailing of reporting requirements and specific dashboard use cases will be refined to support the definition and prioritization of the reporting and dashboard capabilities within the MVP.
